


# Orlo Vista Flood Mitigation

## Project Update



Orange County  
Public Works Department

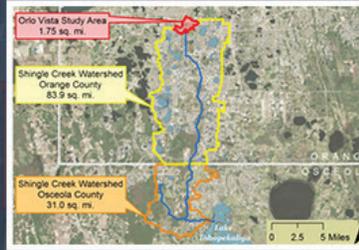

District 6 Commissioner  
Mike Scott

**April 2023**

Greetings Orlo Vista and Westside Manor residents,

Orange County Public Works is pleased to present our Project Update newsletter which provides you with important information about the flood mitigation project. In addition to this April newsletter, Orlo Vista and Westside Manor residents can review meeting presentations, FAQs, and past newsletters online:

<https://www.orangecountyfl.net/OrloVistaWestsideManor>

If you have any questions, please call: **Orange County Public Works • 407-836-7900**

## KEY PROJECT UPDATES

- ▶ The contractor has placed silt fence along the perimeter of the project per plan. They have mobilized construction equipment to the jobsite including a Frontend Loader, Excavator, and End Dump Truck. They have constructed two soil-tracking devices at each entrance gate (Robinson & Livingston).
- ▶ Hoses have been delivered, fused together (this process is time consuming but necessary), and placed in preparation of pumping water. 2- 12" pumps are in place. 2-8" pumps are on site ready to begin pumping water from the North and South ponds into the West Pond.
- ▶ A perimeter fence has been installed around the Eagle's nest on top of Cell Tower.
- ▶ Contractor has begun installing check dams in canal, in preparation for pumping. They have made repairs to existing Type B fence and silt fence that was cut/damaged by people entering site, in South/West corner of project. As soon as the Dewatering Plan is approved by Orange County, they will begin pumping down the North and South ponds.

# KEY PROJECT UPDATES

(CONTINUED)

▶ The contractor has provided photos of the site with key progress indicators. The “comments” section beside each photo explains the location and work completed.

GEOSYNTEC CONSULTANTS Photographic Record		
Client: Orange County Public Works - Stormwater Management Division		Project Number: FW9567
Site Name: Orlo Vista		Site Location: Orlo Vista, Florida
Photograph 1 Date: 4/12/2023 9:02 AM Direction: W Comments: Excavated hole filled on east side of west pond.		
Photograph 2 Date: 4/12/2023 9:03 AM Direction: W Comments: Fused polyethylene pipes connected to pumps lying between west pond and south channel.		

GEOSYNTEC CONSULTANTS Photographic Record		
Client: Orange County Public Works - Stormwater Management Division		Project Number: FW9567
Site Name: Orlo Vista		Site Location: Orlo Vista, Florida
Photograph 3 Date: 4/12/2023 9:04 AM Direction: W Comments: Pumps at south point of west pond.		
Photograph 4 Date: 4/12/2023 9:05 AM Direction: SW Comments: Pumps and pipe connections on weir at south point of west pond.		

## ADDITIONAL SITE PHOTOS

